



Main Campus

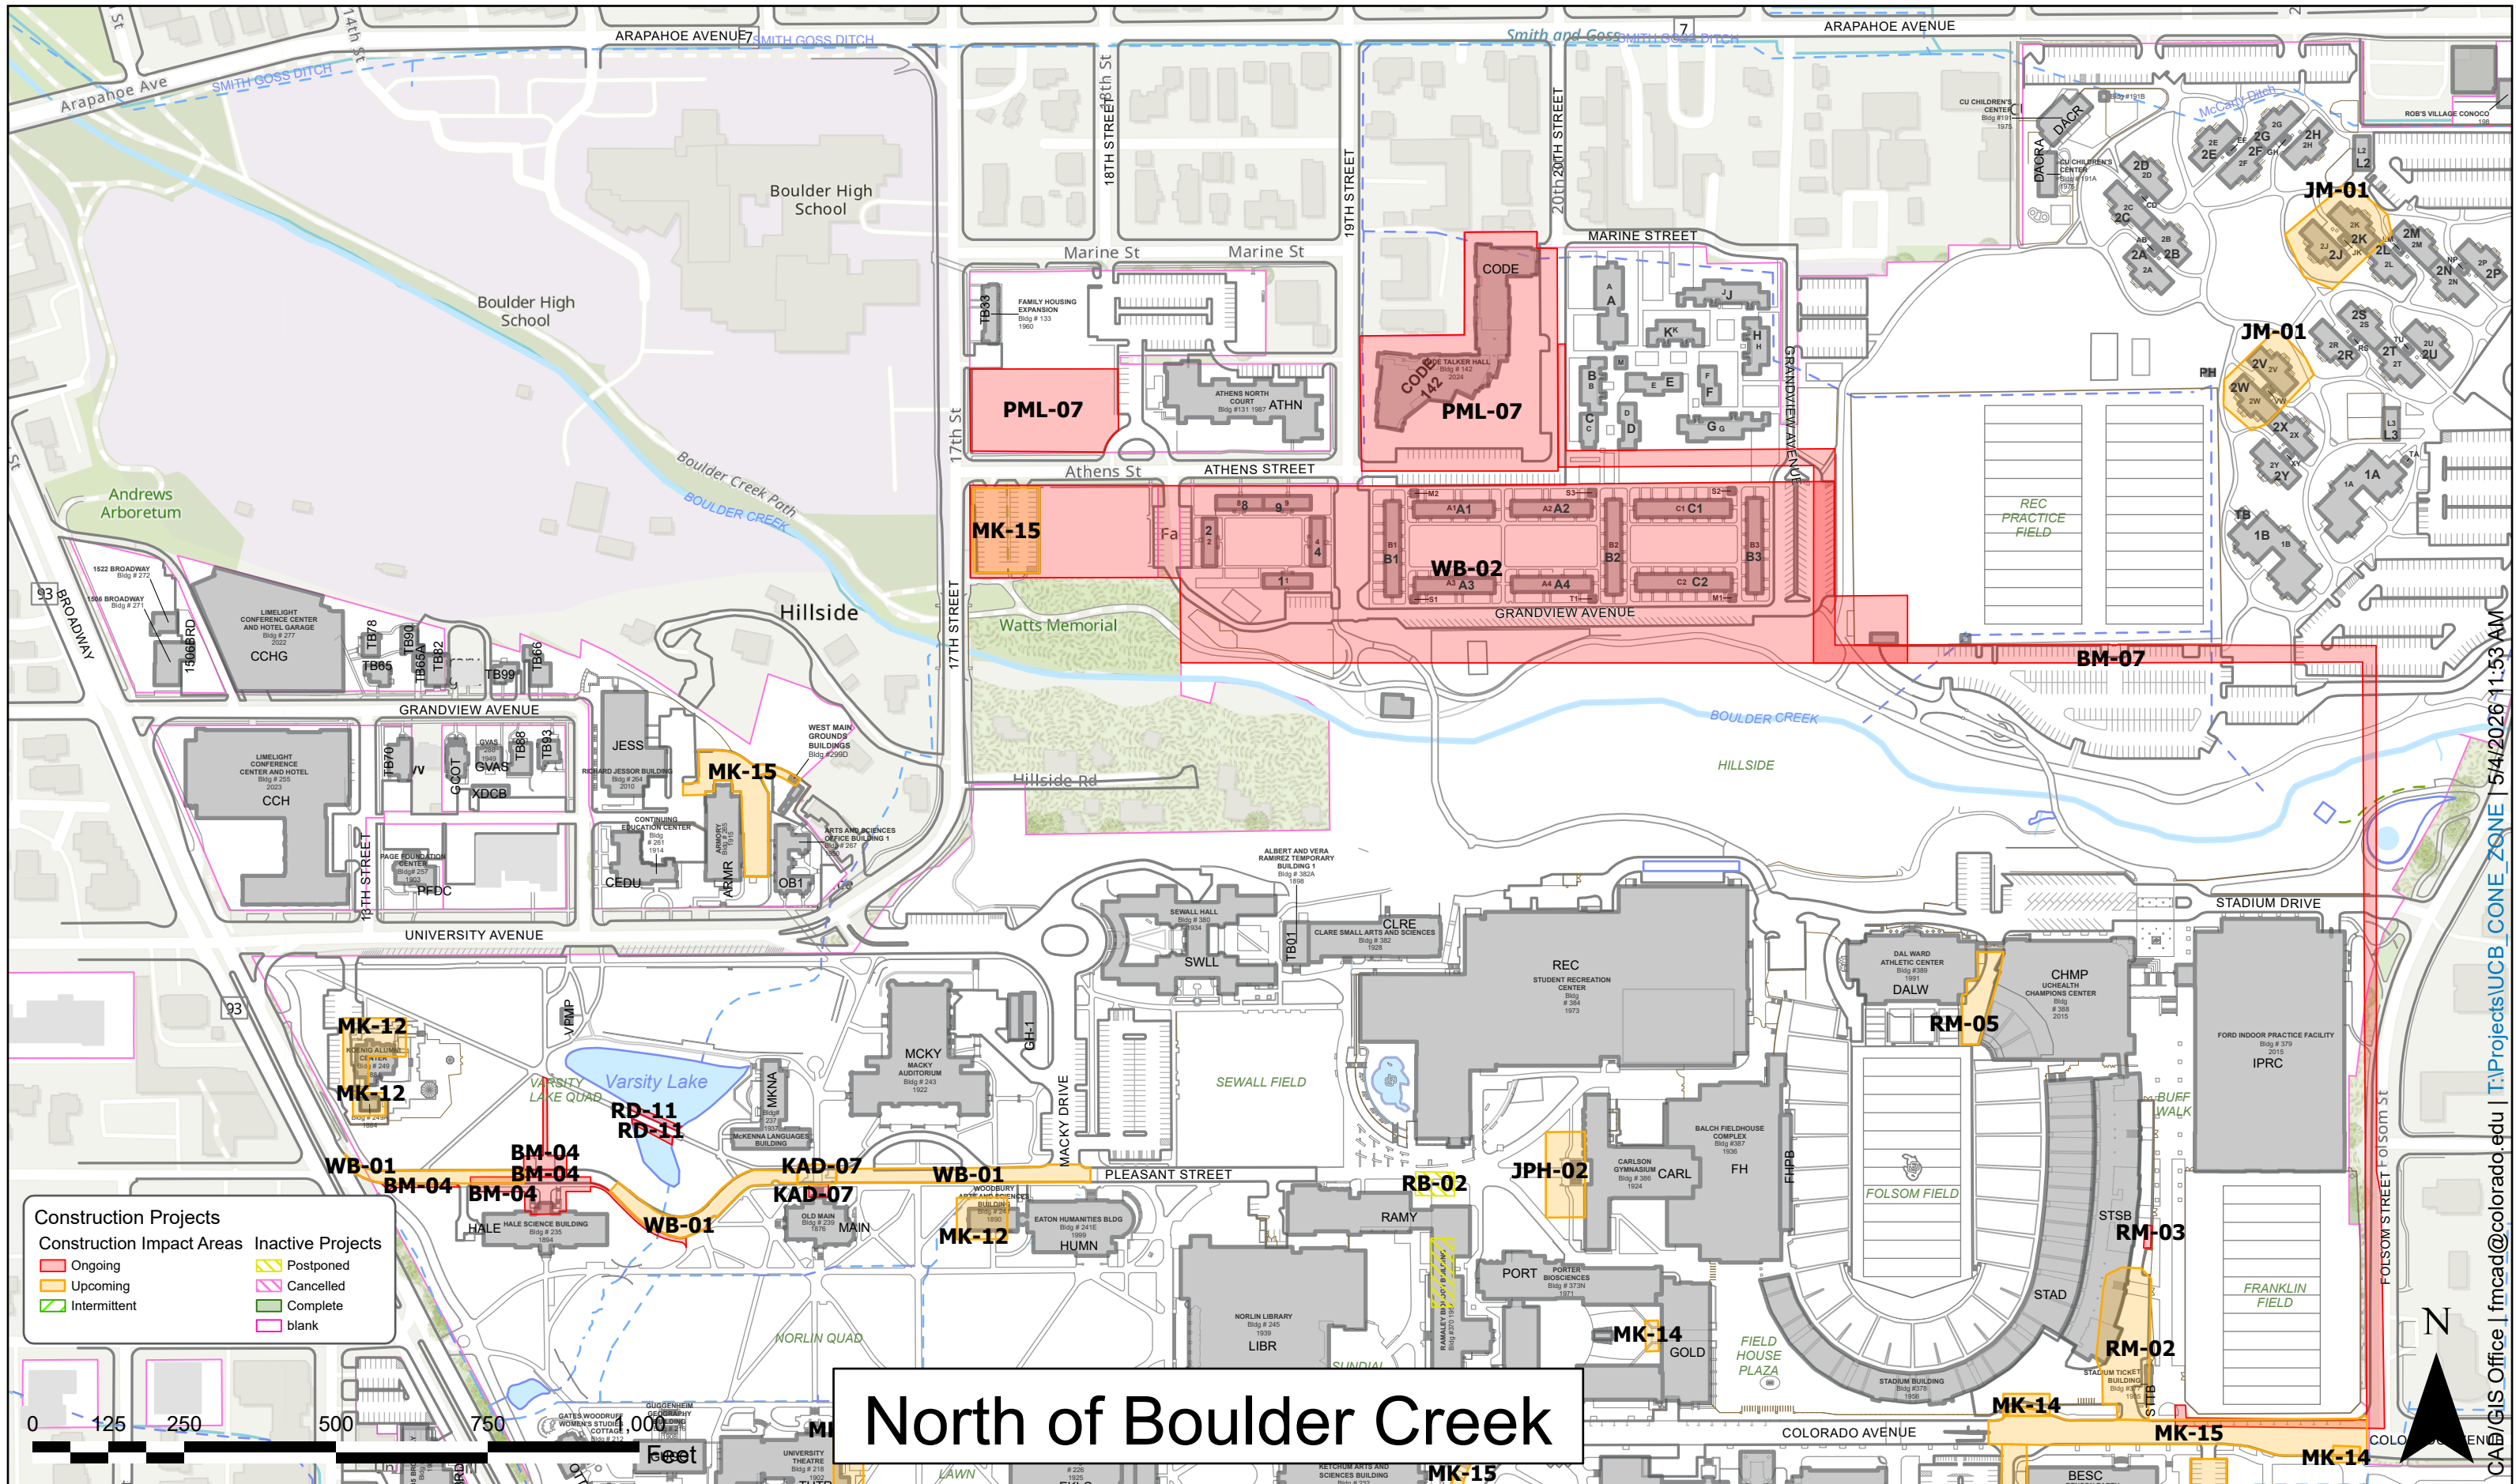

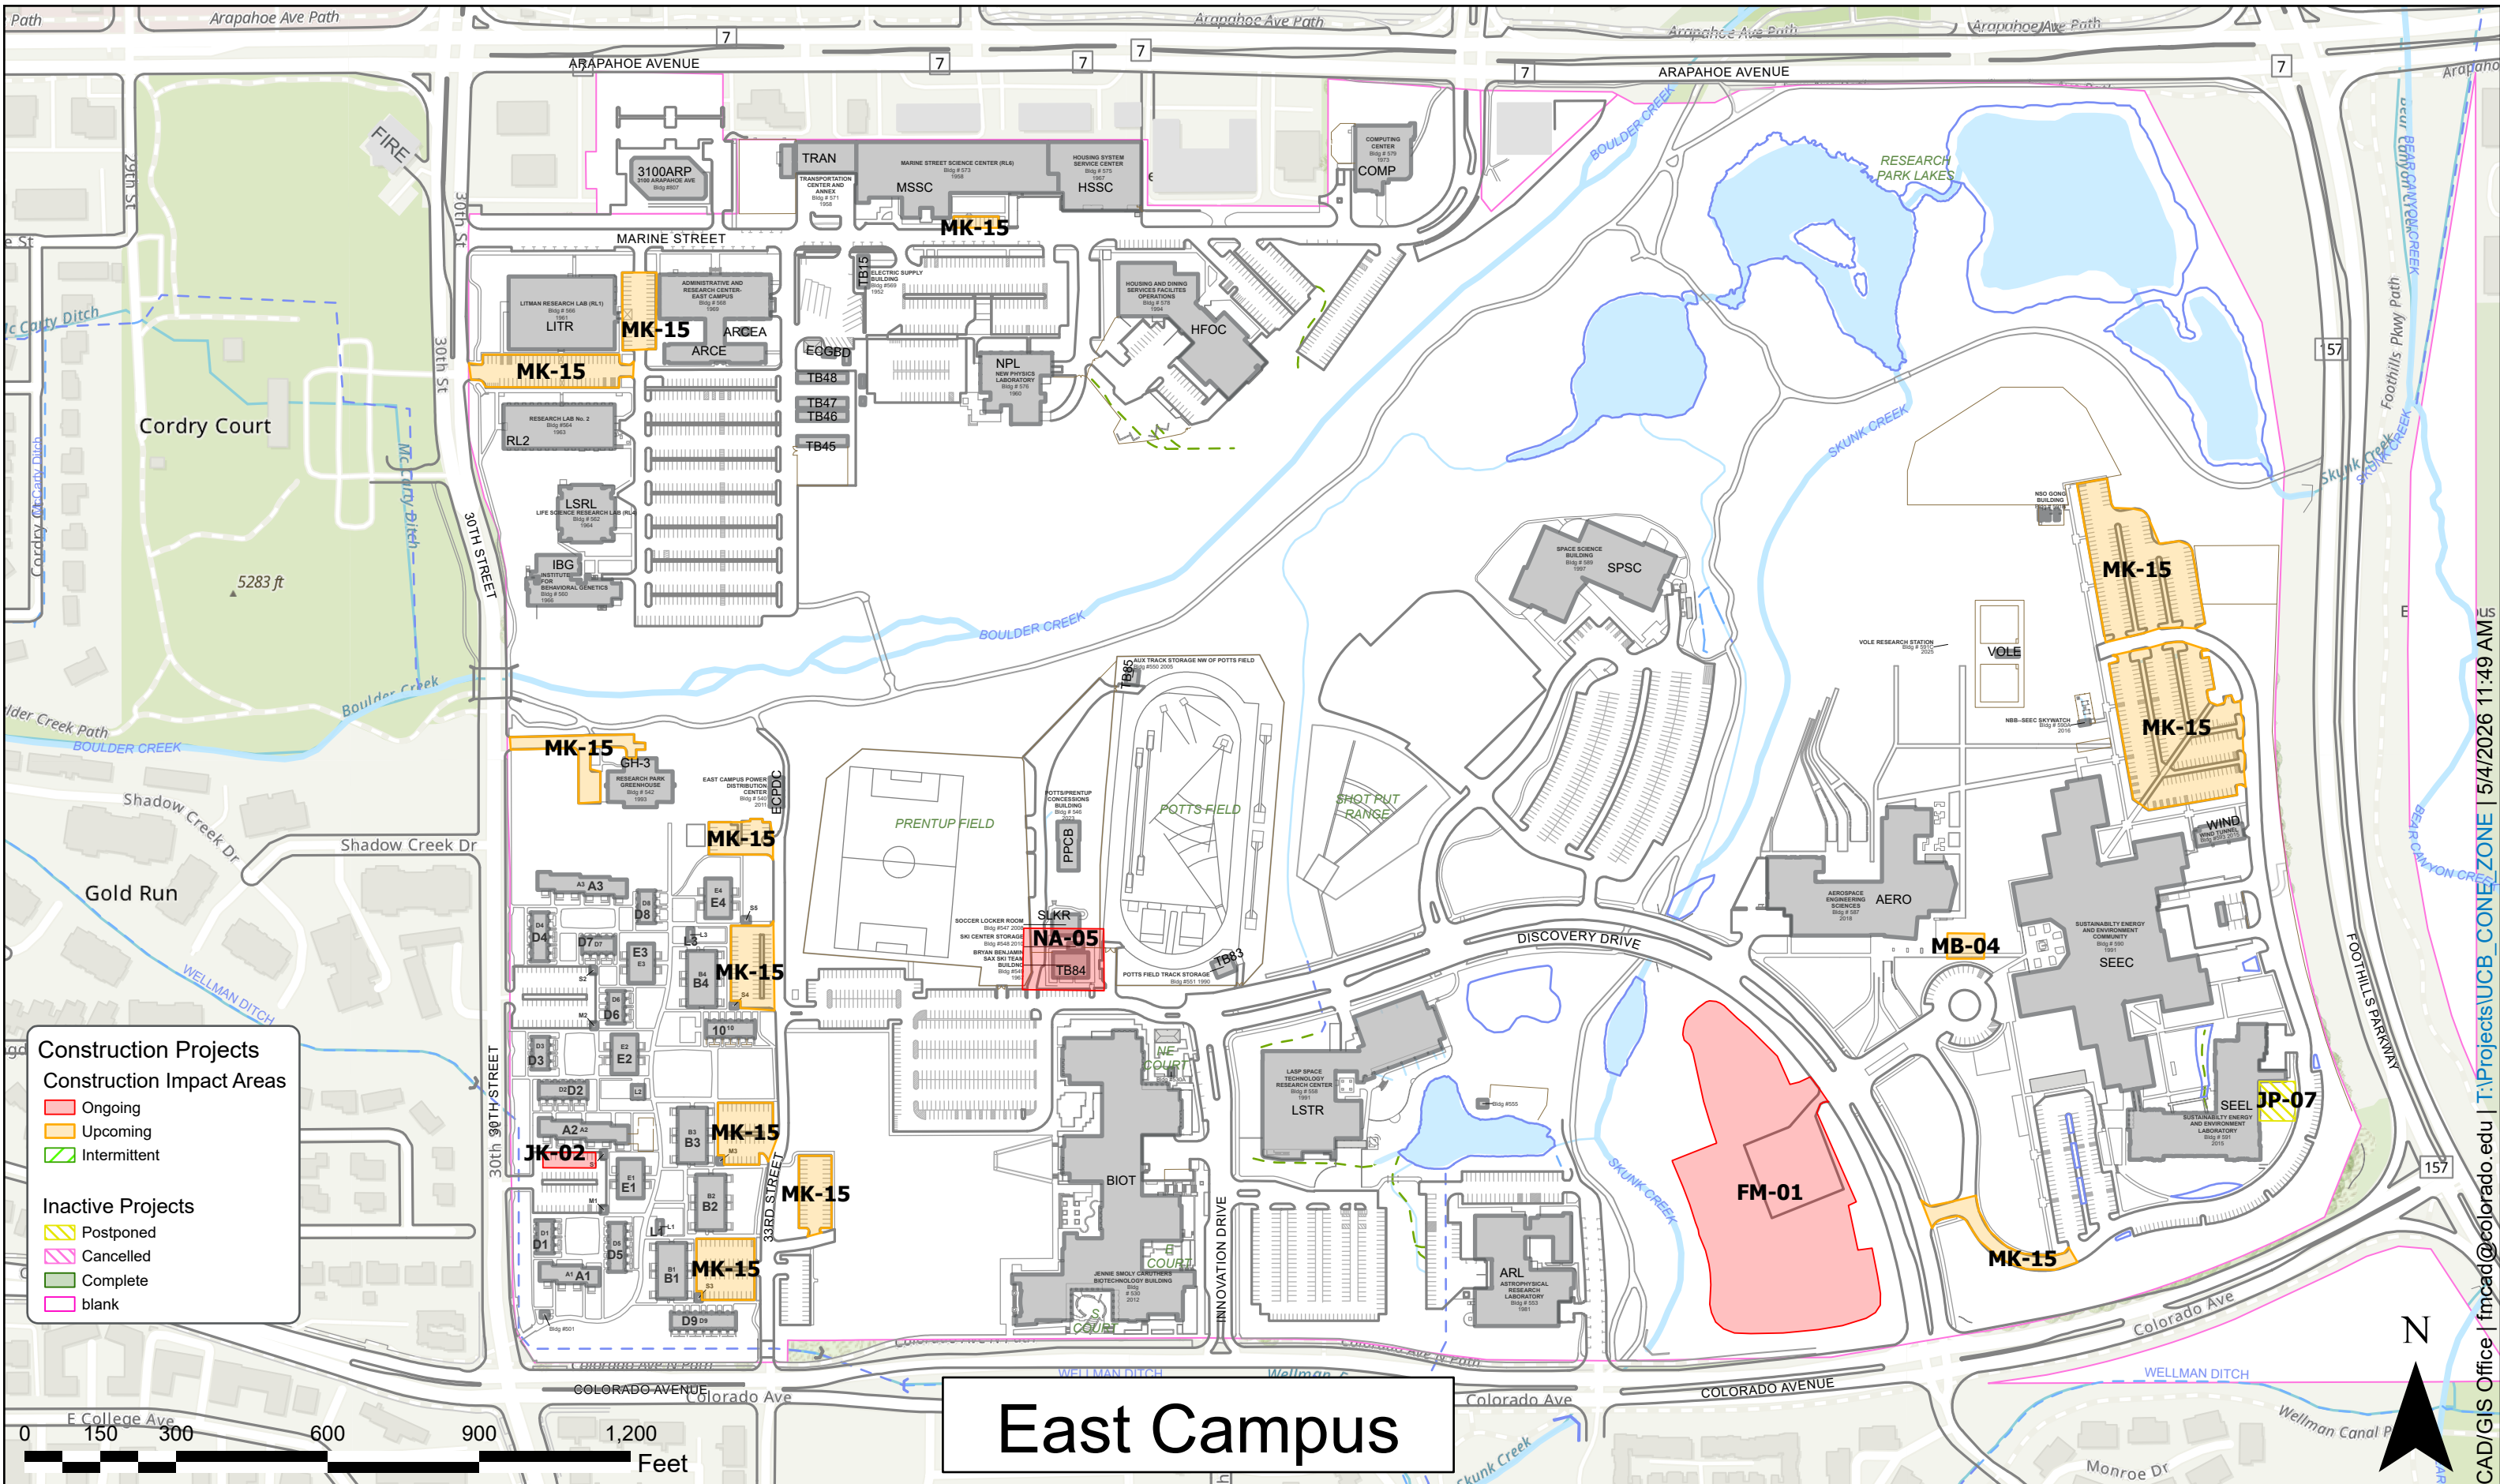

- Construction Projects**
- Construction Impact Areas
 - Ongoing
 - Upcoming
 - Intermittent
- Inactive Projects**
- Postponed
 - Cancelled
 - Complete
 - blank

East Campus

	Project ID	Project Name	Time Frame	Notes	Project Nu	Project Manager
ONGOING	BM-04	HALE - North Entrance Reconstruction	5/1/2025 - Summer 2026	Complete reconstruction of North Entrance underneath North tower of Building. Main Construction to begin Summer 2024. Investigative and shoring work will occur in Summer 2023, Winter Break 23-23 and Spring Break 2024. Pleasant St closure 6/22 - 7/3.	UCB000791	Brian Moffitt
ONGOING	BM-07	SITE - NORTH OF BOULDER CREEK - UTIL	Fall 2024 to May 2026	Utility corridors for Res 1 & parking garages, 4 seperate bid packages meeting with contractor to get project started will have more information coming	UCB000680	Brian Moffitt
ONGOING	DB-02	Chemistry & Applied Math building	Summer 2025 - August 2027	~140,000 SF multi-story building on the Business Field, with basement, utilities and associated site work. Utility work in Regent Drive and Engineering Drive to continue in Summer of 2026.	UCB000762	David Byrne
ONGOING	FM-01	East Campus Construction Staging	ONGOING	East Campus Construction Staging Area	Various	
UPCOMING	FA-01	CHW System Capacity Upgrade	Summer 2026	Impact will be inside the CHAP footprint	UCB001330	Flora Aguirre-Diaz
UPCOMING	FA-02	CHW Expansion to PDPS	Summer 2026	Impact will be a shut down of Regent and most likely in the footprint of the exterior work for CHAP sanitary sewer	UCB001319	Flora Aguirre-Diaz
ONGOING	JK-02	SMCT-ATHN-EV Charging Stations-2023	Spring - Summer 2026	One EV dual head charger will be installed at Smiley Court. One EV space is for Colorado Car Share and one ADA parking spot with access to this EV charger as well.	UCB000996	Jon Keiser
UPCOMING	JPH-02	MULTI-Monumental Stair Upgrades	Late May 2026 - Aug 2026	Stair upgrades to west side of Carlson	UCB001433	Jeff Pfeil
POSTPONED	JP-06	MCPG2-Main Campus #2 Parking Garage	On Hold	New parking garage at existing surface lot north of Regent Parking Garage	UCB000795	Josh Porosky
POSTPONED	JP-07	SEEL NQN Clean Room Addition	ON HOLD: TBD 2026 - TBD 2027	ON HOLD pending NSF approval. Clean room addition to existing SEEL COSINC facility	UCB001167	Josh Porosky
ONGOING	KAD-07	Old Main Structural and Exterior Repairs	Pleasant St closure at Old Main: July 6 - July 31	Coord. with Hale closure and mill/overlay project. Will use Macky Loop for a traffic loop. Would like to purchase the parking spots during this period.	UCB000255	Katherine Dunklau
ONGOING	KAD-08	WSTE-Sewage Treatment System Repairs (Mountain Research Station)	Finish August 2026	Work restarting	UCB001154	Katherine Dunklau
POSTPONED	MB-03	SITE-Lot 306-Upgrade EV Charging Infrastructure	ON HOLD	Install three EV charging stations in lot 306	UCB001282	Matt Buck
UPCOMING	MB-04	AERO-Libraries Outdoor Pick Up and Return Locker	June 2026 - July 2026	Installation of electronic book lockers near roundabout between SEEC and AERO	UCB001404	Matt Buck
UPCOMING	MK-12	Multi-Envelope Painting FY 25-26 (DM)	June 2026	Exterior Painting at Woodbury, Alumni (and Garage), and east side of Theater	UCB001514	Mykala Keuter
ONGOING	MK-13	Multi-Replace ATMs	April - May 2026	Replacement of ATMs near Libby and Stearns West	UCB001505	Mykala Keuter
UPCOMING	MK-14	SITE-Non-Emergency Civil Utility Repairs-FY26	June - August 2026	Various civil utilites reapirs to drains, storms, etc.	UCB001422	Mykala Keuter

	Project ID	Project Name	Time Frame	Notes	Project Nu	Project Manager
UPCOMING	MK-15	SITE-Asphalt Maintenance Repairs FY26	May - August 2026	Various parking lot and street asphalt repairs/replacements	UCB001469	Mykala Keuter
UPCOMING	NA-03	Wolf Law Gutters and Downspouts	April 2026	Two contractors are currently coordinating schedules to get out on site this month.	UCB000540	Nicole Arena
UPCOMING	NA-04	EKLC - Waterline / Sewer Repairs	Summer 2026	Construction awarded to Goodland. Project starting May 11th with impact between Cristol and Ekeley. Project outage going out week of 4/6	UCB000464	Nicole Arena
ONGOING	NA-05	SITE - Irrigation Mainline Upgrades	March 2026 - April 2026	Phase two has started. Work is along Discovery Dr. near Prentup Field. Coordinating with Athletics to make sure impact is minimal, project should be complete by end of April.	UCB000855	Nicole Arena
UPCOMING	NA-06	Multi-Remove or Repair Exterior Fire Escapes	March 2026 - April 2026	Work at Bruce Curtis to be scheduled this spring. Outage should be small and close to the building, not expecting any sidewalk closures.	UCB001160	Nicole Arena
ONGOING	PM-06	MULTI WV-HHW Conversion Phase I & II	May 2026 - August 2026	Install new HHW heating lines to Bear Creek buildings, additional phases will include Village Center, Darley, Stearns and WillVill North.	UCB000612	Patricia McNally-Leef
ONGOING	PM-07	Residence One	April 2024-August 2026	Project will build a new apartment style residence hall containing 95 units, a UPS store, and a cafe/grab and go, within the facility. Project is in construction.	UCB000393	Patricia McNally-Leef
UPCOMING	PM-08	WV - Clean Thermal Energy Transition -Phase 2	July 2026 - August 2026	Parking area will be out south of Williams Village	UCB001333	Patricia McNally-Leef
POSTPONED	RB-02	RAMY C490 Refurbish SF2 and AHU2	Summer delayed to 2027 - may be done earlier if a fan failure creates an	Crane from north side TBD, if needed - Plan to be finalized - may be delayed...	UCB001039	Rachael Bray
UPCOMING	RB-03	DLC Interior Project	May 2026 - December 2026	Staging area for DLC Work in the loading dock area and surroundings	UCB001259	Rachael Bray
UPCOMING	RB-04	MULTI Campus Security	Summer 2026 - December 2026	Exterior camera installations - various locations, approx. 35 buildings (1st phase - 3 on east campus and 4 on main campus)	UCB001402	Rachael Bray
ONGOING	RD-11	SITE-Varsity Pond Bridge & Dam Repairs	June 2025 - July 2025 May 2026	Scope has been reduced and will be doing minor repairs on the bridge and damn	UCB000463	Richard Dencklau
UPCOMING	RD-12	SITE-Reconfigure Lot 440	April-July 2025	New entry into lot to be installed in April, all other changes to happen after CHAP sanitary line installed	UCB001463	Richard Dencklau
UPCOMING	RM-02	STSB - RF700 & RF800 - Remove and Replace Wind Damaged Roofs	May 2026 - August 2026	Only impacts to campus will be weekend days when we are removing demo'd roof material or picking new material to level-8 roof of STSB. Still TBD on crane dates - determined once contract is executed	UCB001510	Ryan Moeller
ONGOING	RM-03	STSB-RM 768 Stadium Skybox Suite Renovation	December 1, 2025 - June 30, 2026	The only impact to Franklin Drive will be access to the passenger elevator up to level-7 of STSB as well as a dumpster staged north of the emergency generator on Franklin	UCB001299	Ryan Moeller

	Project ID	Project Name	Time Frame	Notes	Project Nu	Project Manager
ONGOING	RM-05	DALW - North Videoboard & Ribbon Board Upgrade	3/30/26 - 5/31/26	Existing north and field boards being removed and replaced. Crane work complete. Parking lot due north of Gate 14 will be intermittently taken offline for crane logistics and material deliveries	UCB001509	Ryan Moeller
UPCOMING	WB-01	SITE - Pleasant Street Mill and Overlay	August 2026	Mill and overlay of Macky Drive to be done at the same time as Old Main and Hale work	UCB001524	Ward Bauscher
ONGOING	WB-02	SITE-NBC Overhead Utilities Relocation	Summer 2026	Mill and overlay of Macky Drive to be done at the same time as Old Main and Hale work. Road closure 8/3 - 8/7.	UCB001396	Ward Bauscher
UPCOMING	JK-02	FRND-Renovation-2026	June 1, 2026 - July 1, 2028	Major renovation, construction fence aro	UCB001046	David Benjes
UPCOMING	JM-01	NTCT 2R, 2V & 2W-Exterior Balcony Removal-2026	May 18, 2026 - July 31, 2026	Buildings 2R, 2V, 2W and 2S will have the existing balconies removed. Demolition/removal of existing Twin Tee balconies, install new juliet railing, remove existing wood fence at grade and build new wood fence in same location. Construction fence will move and be adjusted based on the work at each building and will be removed as soon as demolition/construction work is complete	UCB001460	John Mott
